



Sella

● Group 1.

● Outline

- Introduction
- Problem statement
- Methodology with justification
- Project charter
- Technique for collecting requirement

● Outline

- Project requirement
- Project scope
- WBS & WPS dictionary
- Gantt chart
- RACI chart

Introduction



In recent years, entrepreneurship has grown significantly and has become an important contributor to economic development. Startups introduce innovative ideas, products, and services to the market, which helps create new opportunities and support business growth. However, one of the main challenges entrepreneurs face is finding the right investor to support their projects financially and strategically.

At the same time, investors are constantly looking for promising startups that match their interests and investment goals. Although there are networking events, incubators, and online platforms that aim to connect both parties, the process is still not fully organized or efficient. Most connections depend on personal relationships or informal communication channels.

With the increasing reliance on digital solutions, there is an opportunity to improve this process by developing a structured and centralized platform that simplifies communication between entrepreneurs and investors.

This project proposes the development of Sella, a smart digital platform designed to enhance investment matching and make the connection process more organized, transparent, and effective.

Problem Statement

● PROBLEM 1

1. Difficulty finding the right match:
Startups struggle to reach investors that fit their business field, funding stage, or investment goals.
Likewise, investors often miss opportunities that suit their interests.

● PROBLEM 2

2. Dependence on personal connections:
Many entrepreneurs rely only on their personal networks, which limit access and creates unfair chances for others.

● PROBLEM 3

3. Unclear or missing information:
Project and investor details are often incomplete or presented differently across platforms, making it hard to evaluate opportunities.

Problem Statement

● PROBLEM 4

4. No clear classification system:
There is no organized way to filter or group startups and investors by sector, size, or growth stage, which wastes time and effort.

● PROBLEM 5

5. Lack of tracking and analytics:
Current methods don't allow users to track meetings, monitor interest levels, or analyze trends in investment activity.

Methodology with justification

The Sella project is going to use the Agile Software Development Life Cycle and the Scrum framework to develop the platform. We chose the method because it allows us to be flexible and make improvements as we go along. This is important for platform.

The Sella platform is a platform that connects entrepreneurs with investors. The needs of the system can change over time because of feedback from the people who use the Sella platform and what is happening in the market. There are also changes in regulations that can affect the platform. The Agile method helps the development team deal with these changes without stopping the project.

Project charter



صلة

Project Charter

Project Title: Sella

Date of Authorization: March 7, 2026

Project Start Date: March 7, 2026

Projected Finish Date: July 15, 2026

Key Schedule Milestones:

- Complete detailed requirements and system design by April 1.
- Develop the core matching engine and MVP by June 15.
- Complete pilot testing and final production version by July 15.

Budget Information:

The allocated budget for this project is \$150,000. These funds cover internal development labor, algorithm design, and UI/UX. Marketing and legal compliance for investment data will be outsourced as needed.

Project Manager:

Renad Amuhaysini, +996503900707, R.almuhaysini@gmail.com.

Project Objectives:

The objective is to develop a centralized digital platform that automates the connection between startups and investors. The project aims to replace unstructured networking with a smart matching system that simplifies fundraising in four months.

Project Success Criteria:

The platform must accurately match users based on pre-defined criteria, pass all security audits for financial data, and be completed within the \$150,000 budget. Success is defined by official sponsor approval and positive feedback from initial beta testers.

Approach:

- Use an Agile development methodology with two-week sprints.
- Develop a Work Breakdown Structure (WBS) and Gantt chart within the first month.
- Hold weekly progress review meetings with the core team and the sponsor.
- Conduct thorough security and usability testing before the pilot launch.

Name	Role	Position	Contact Information	Signature
Sultanah Almughamis	Sponsor	CEO	sultanahibrahim23@gmail.com	
Renad Almuhsayni	Project Manager	Project Manager	R.almuhaysini@gmail.com	
Fajr alrubeaan	Team Member	Developer	alrubeaanfajer@gmail.com	
Renad alsubaibany	Team Member	Developer	Renadsuh@icloud.com	
Ghadi Alhazzaa	Team Member	Team Member	ghadialhazzaa@gmail.com	
Leeda Alshehri	Team Member	Team Member	leeda.abdullah@yahoo.com	

Sponsor Authority:

The sponsor provides overall direction, approves major scope or budget changes, and ensures alignment with national investment goals.

Project Manager Authority:

The PM is responsible for daily operations, resource allocation, and approving operational decisions. Budget variances over 10% require sponsor approval.

Comments:

Sella is a critical step toward a more transparent investment ecosystem. I expect the team to prioritize data security and algorithm accuracy above all else." — Project Sponsor. "All system architecture plans are finalized. We're ready to begin the first sprint focusing on the management system." — Project Manager.

Techniques for Collecting Requirements

- **Investors:** Conduct one-on-one interviews to tailor the Smart Matching System to individual financial goals and risk levels.
- **PNU Student Entrepreneurs:** Use digital surveys to identify the pain points and needs of a high volume of student founders quickly.
- **Project Sponsors:** Organize focus groups to ensure the platform's vision aligns with national investment goals and leadership expectations.
- **App Development Team:** Use interactive prototyping to refine the Sella dashboard and catch design flaws before the coding phase.
- **Technical Support & Security:** Utilize process observation to build robust security protocols for protecting sensitive financial data.
- **Marketing Team:** Perform market benchmarking against global platforms to refine requirements and ensure Sella's competitive edge.

Project Requirements



Functional Requirements

- Smart Matching: AI-driven connections between startups and investors.
- Live Updates: Real-time notifications for matches and interest alerts.
- Unified Dashboard: Organized views for matches, profiles, and meetings.
- Advanced Search: Precise filtering by industry, stage, and company size.
- Bilingual Support: Seamless toggle between Arabic and English.
- Support Chat: Instant assistance via live chat or AI bot.

Non-Functional Requirements

- Speed: High-performance processing with zero lag.
- Scalability: Capacity to handle thousands of concurrent users.
- Security: Multi-factor authentication (MFA) and strong encryption.
- Availability: 99.9% uptime for consistent platform access.
- Usability: Professional interface with a simple learning curve.
- Compliance: Full adherence to privacy laws and financial regulations.

Software Requirements

- Matching Engine: Specialized algorithms for automated networking.
- Database Management: Secure system for profiles and platform activity.
- Identity Verification: Robust framework for verified professional access.
- Document Vault: Encrypted space for pitch decks and business plans.
- Scheduling Tools: Integrated booking and notification systems.

Hardware Requirements

- Hosting Infrastructure: Reliable servers for smooth iOS and Android performance.
- Security Servers: Dedicated hardware for encrypted financial records.
- Network Defense: Professional firewalls and 24/7 monitoring systems.



Project scope statement

Project Scope Description:

The Sella project aims to develop a web-based platform that connects entrepreneurs with investors in an organized and efficient way. The platform will allow users to present projects, explore opportunities, and communicate through a centralized system that includes user management, project submission, a matching system, dashboards, and communication tools.

Project Exclusions:

- Mobile application
- Integration with external financial or banking systems.
- Real-time funding transactions or payment processing.
- Advanced AI prediction models beyond basic matching.
- Long-term platform maintenance after delivery.

Project Assumptions:

- Users have internet access.
- Users are willing to create and manage profiles.
- Provided data by users is accurate.
- The platform will be used in a controlled academic environment

Project Constraints:

- Limited project duration (semester timeline).
- Limited resources and tools.
- Team size and skill levels.

Project Deliverables:

- Fully functional Sella platform (web-based system).
- System documentation.
- Testing and evaluation report.
- Final presentation.
- Basic analytics and tracking features.

Project Acceptance Criteria:

- Users can successfully register and log in to the platform.
- Entrepreneurs can create and submit project profiles.
- Investors can browse and filter projects easily.
- The matching system provides relevant suggestions.
- Users can schedule meetings through the platform.
- Notifications are sent and received correctly.
- The system operates without major errors or crashes.
- The platform meets usability and functionality requirements.
- The system passes testing and validation processes.



Project Scope Statement

Project Title: Sella.

Date of Prepared: April 17, 2026

Project Scope Description:

The Sella project aims to develop a web-based platform that connects entrepreneurs with investors in an organized and efficient way. The platform will allow users to present projects, explore opportunities, and communicate through a centralized system that includes user management, project submission, a matching system, dashboards, and communication tools.

Project Deliverables:

- Fully functional Sella platform (web-based system).
- System documentation.
- Testing and evaluation report.
- Final presentation.
- Basic analytics and tracking features.

Project Acceptance Criteria:

- Users can successfully register and log in to the platform.
- Entrepreneurs can create and submit project profiles.
- Investors can browse and filter projects easily.
- The matching system provides relevant suggestions.
- Users can schedule meetings through the platform.
- Notifications are sent and received correctly.
- The system operates without major errors or crashes.
- The platform meets usability and functionality requirements.
- The system passes testing and validation processes.

Project Exclusions:

- Mobile application
- Integration with external financial or banking systems.
- Real-time funding transactions or payment processing.
- Advanced AI prediction models beyond basic matching.
- Long-term platform maintenance after delivery.

Project Constraints:

- Limited project duration (semester timeline).
- Limited resources and tools.
- Team size and skill levels.
- Academic requirements and deadlines.

Project Assumptions:

- Users have internet access.
- Users are willing to create and manage profiles.
- Provided data by users is accurate.
- The platform will be used in a controlled academic environment.

WBS

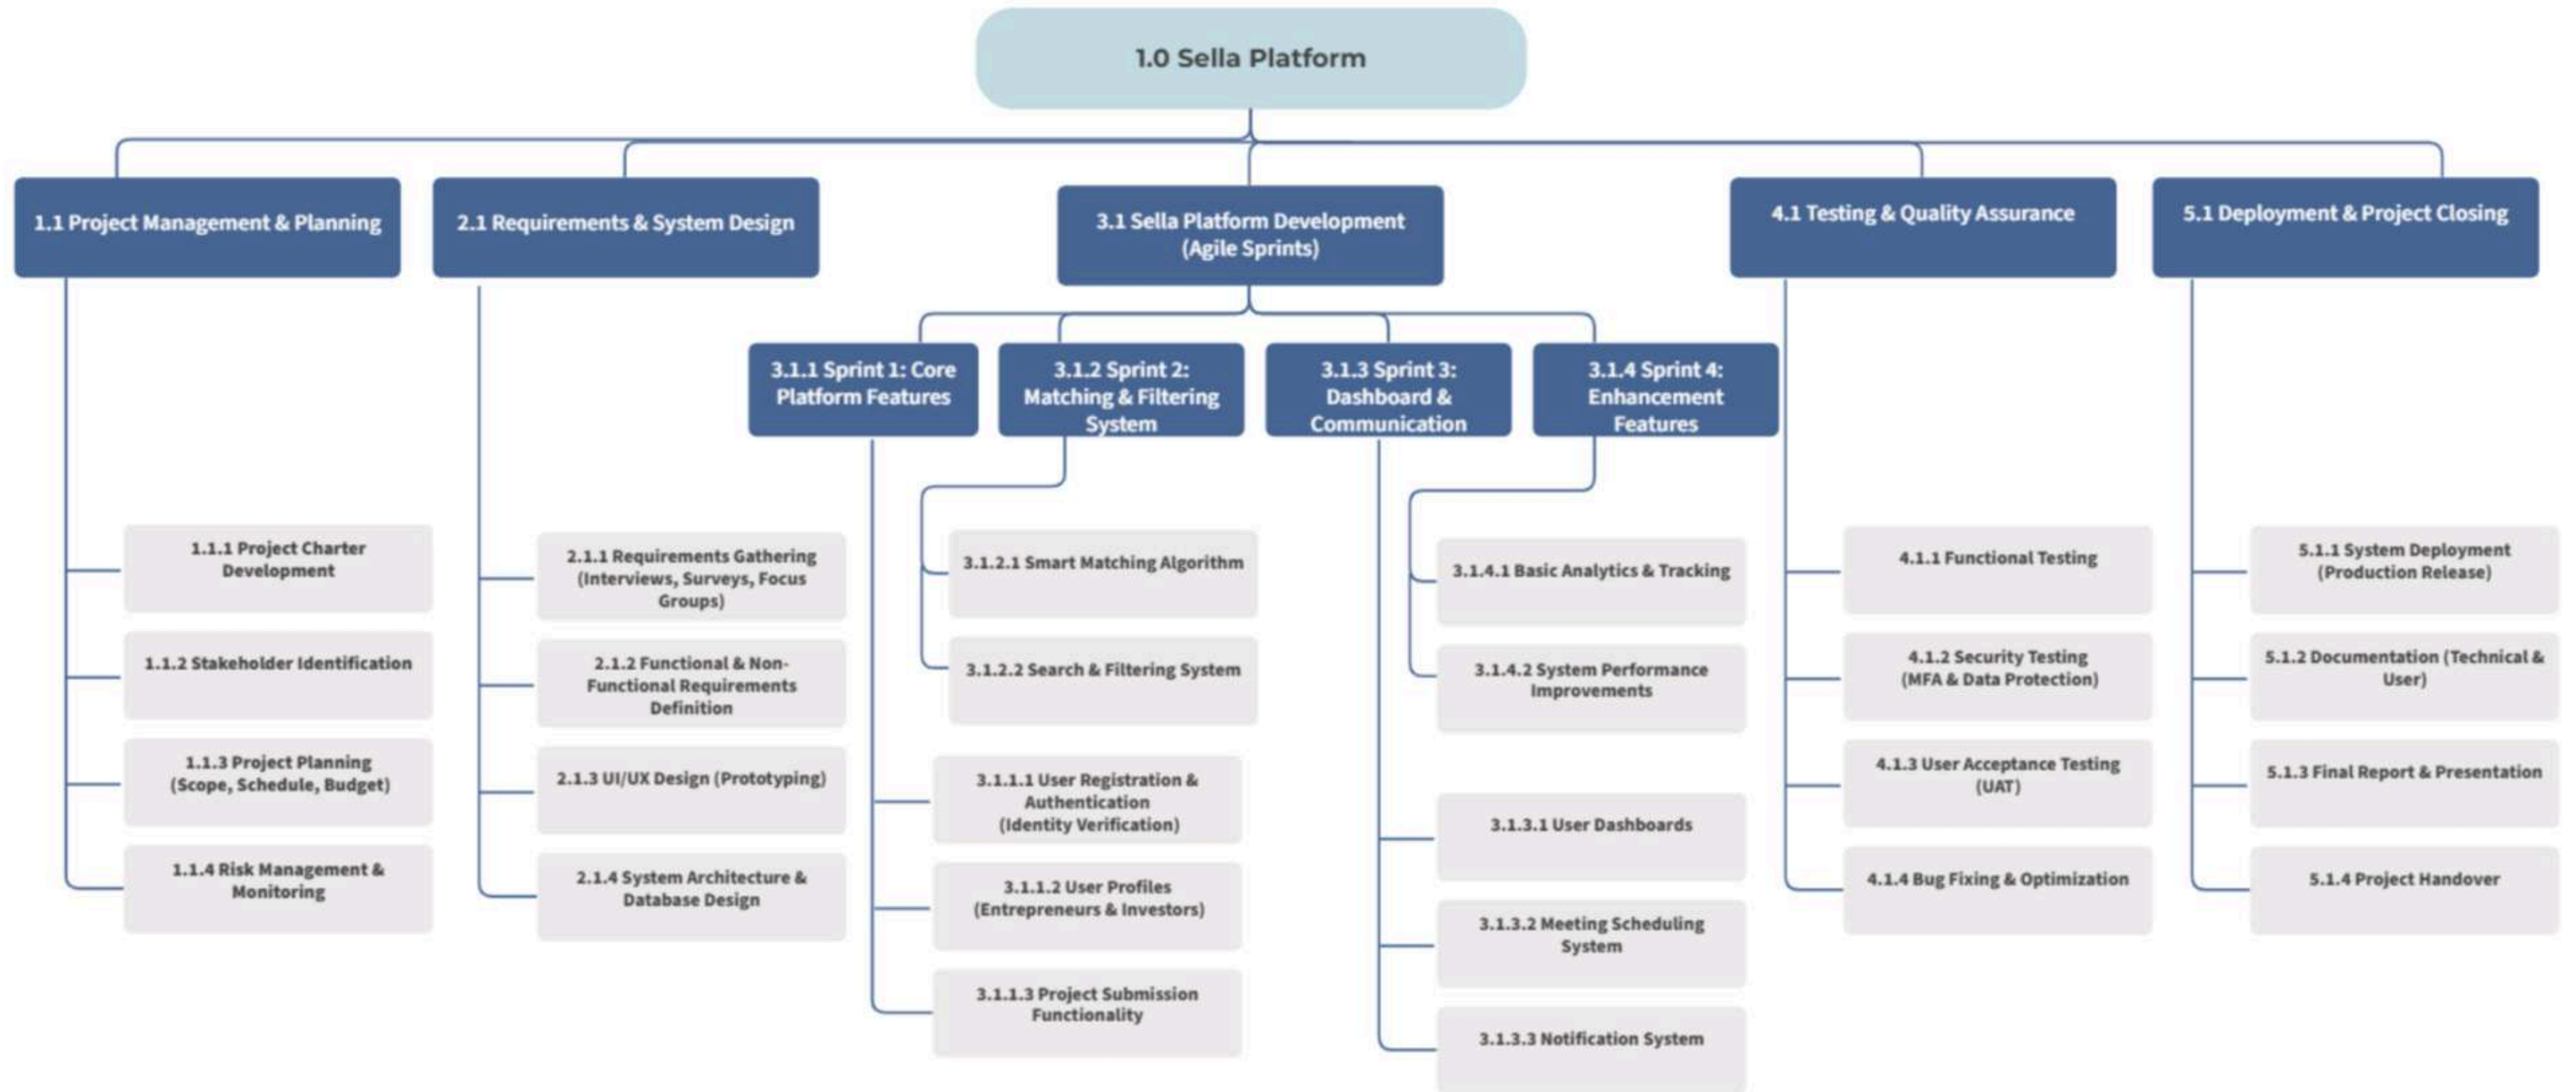


Figure 4: WBS of Sella Platform

WBS Dictionary


WBS	Work Description	Activities	Required Resources	Cost Estimates	Acceptance Criteria	Responsible Manager
1.1.1	Develop project charter for Sella platform	Define objectives, scope, stakeholders	Project team, documentation tools	Low	Approved project charter completed	Project Manager
1.1.2	Identify stakeholders	List entrepreneurs, investors, sponsors	Project team	Low	Stakeholder list completed	Project Manager
2.1.1	Collect system requirements	Interviews, surveys, focus groups	Stakeholders, survey tools	Low	Requirements document completed	Business Analyst
2.1.2	Define functional & non-functional requirements	Analyze and document requirements	Project team	Low	Requirements specification approved	Business Analyst
2.1.3	Design UI/UX for platform	Wireframes and prototyping	Design tools (Figma)	Medium	Approved UI prototype	UI/UX Designer
2.1.4	Design system architecture & database	Define system structure and database	Developers	Medium	System design completed	System Architect
3.1.1.1	Develop registration & authentication	Login system and identity verification	Developers, database	Medium	Users can register/login securely	Development Team Lead
3.1.1.2	Develop user profiles	Create entrepreneur & investor profiles	Developers	Medium	Profiles created successfully	Development Team Lead
3.1.1.3	Develop project submission feature	Forms and database storage	Developers, database	Medium	Projects submitted successfully	Development Team Lead
3.1.2.1	Develop smart matching system	Matching logic implementation	Developers	Medium	Accurate matching results	Development Team Lead
3.1.2.2	Develop search & filtering	Filtering by sector/stage	Developers	Medium	Filtering works correctly	Development Team Lead
3.1.3.1	Develop user dashboards	Dashboard interface design	Developers	Medium	Data displayed clearly	Development Team Lead
3.1.3.2	Develop meeting scheduling	Scheduling interface and logic	Developers	Low–Medium	Meetings scheduled successfully	Development Team Lead

3.1.3.3	Develop notification system	Alerts and notifications	Developers	Low–Medium	Notifications sent correctly	Development Team Lead
3.1.4.1	Develop analytics & tracking	Basic tracking and reports	Developers	Medium	Analytics displayed correctly	Development Team Lead
4.1.1	Perform functional testing	Execute test cases	QA team	Low–Medium	System functions correctly	QA Manager
4.1.2	Perform security testing	MFA and data protection testing	QA team	Medium	No critical security issues	QA Manager
4.1.3	Conduct user acceptance testing	User testing sessions	Users, QA team	Low	Users approve system	QA Manager
4.1.4	Fix bugs and optimize system	Debugging and optimization	Developers	Medium	System stable and optimized	Development Team Lead
5.1.2	Prepare documentation	Technical and user guides	Project team	Low	Documentation completed	Project Manager
5.1.3	Prepare final report & presentation	Report writing and slides	Project team	Low	Submitted successfully	Project Manager
5.1.4	Project handover and closure	Final delivery	Project team	Low	Project closed officially	Project Manager

RACI Chart

Task	Project Manager	Business Analyst	UI/UX Designer	Development Team	Technical Support & Security	QA Tester	Marketing Specialist	Legal Advisor	End User
Analyze market needs	A	R	I	I	I	I	C	I	C
Identify stakeholders	A	R	I	I	I	I	I	I	C
Define requirements	A	R	I	C	C	C	I	I	I
Design UI/UX	A	C	R	C	I	I	I	I	C
Design system architecture	A	C	I	R	C	C	I	I	I
Develop authentication system	A	C	I	R	C	C	I	I	I
Develop user profiles	A	C	I	R	I	C	I	I	I
Develop project submission	A	C	I	R	I	C	I	I	I
Develop smart matching	A	C	I	R	I	C	I	I	C
Develop search & filtering	A	C	I	R	I	C	I	I	I
Develop dashboards	A	I	C	R	I	C	I	I	I
Develop meeting scheduling	A	I	I	R	I	C	I	I	C
Develop notification system	A	I	I	R	I	C	I	I	I
Develop analytics	A	C	I	R	I	C	I	I	I
Perform functional testing	A	I	I	C	I	R	I	I	I
Perform security testing	A	I	I	I	R	C	I	I	I
Conduct user acceptance testing	A	I	I	I	I	C	I	I	R
Fix bugs & optimization	A	I	I	R	I	C	I	I	I
Launch platform	A	I	I	R	C	C	C	I	I

Gantt Chart

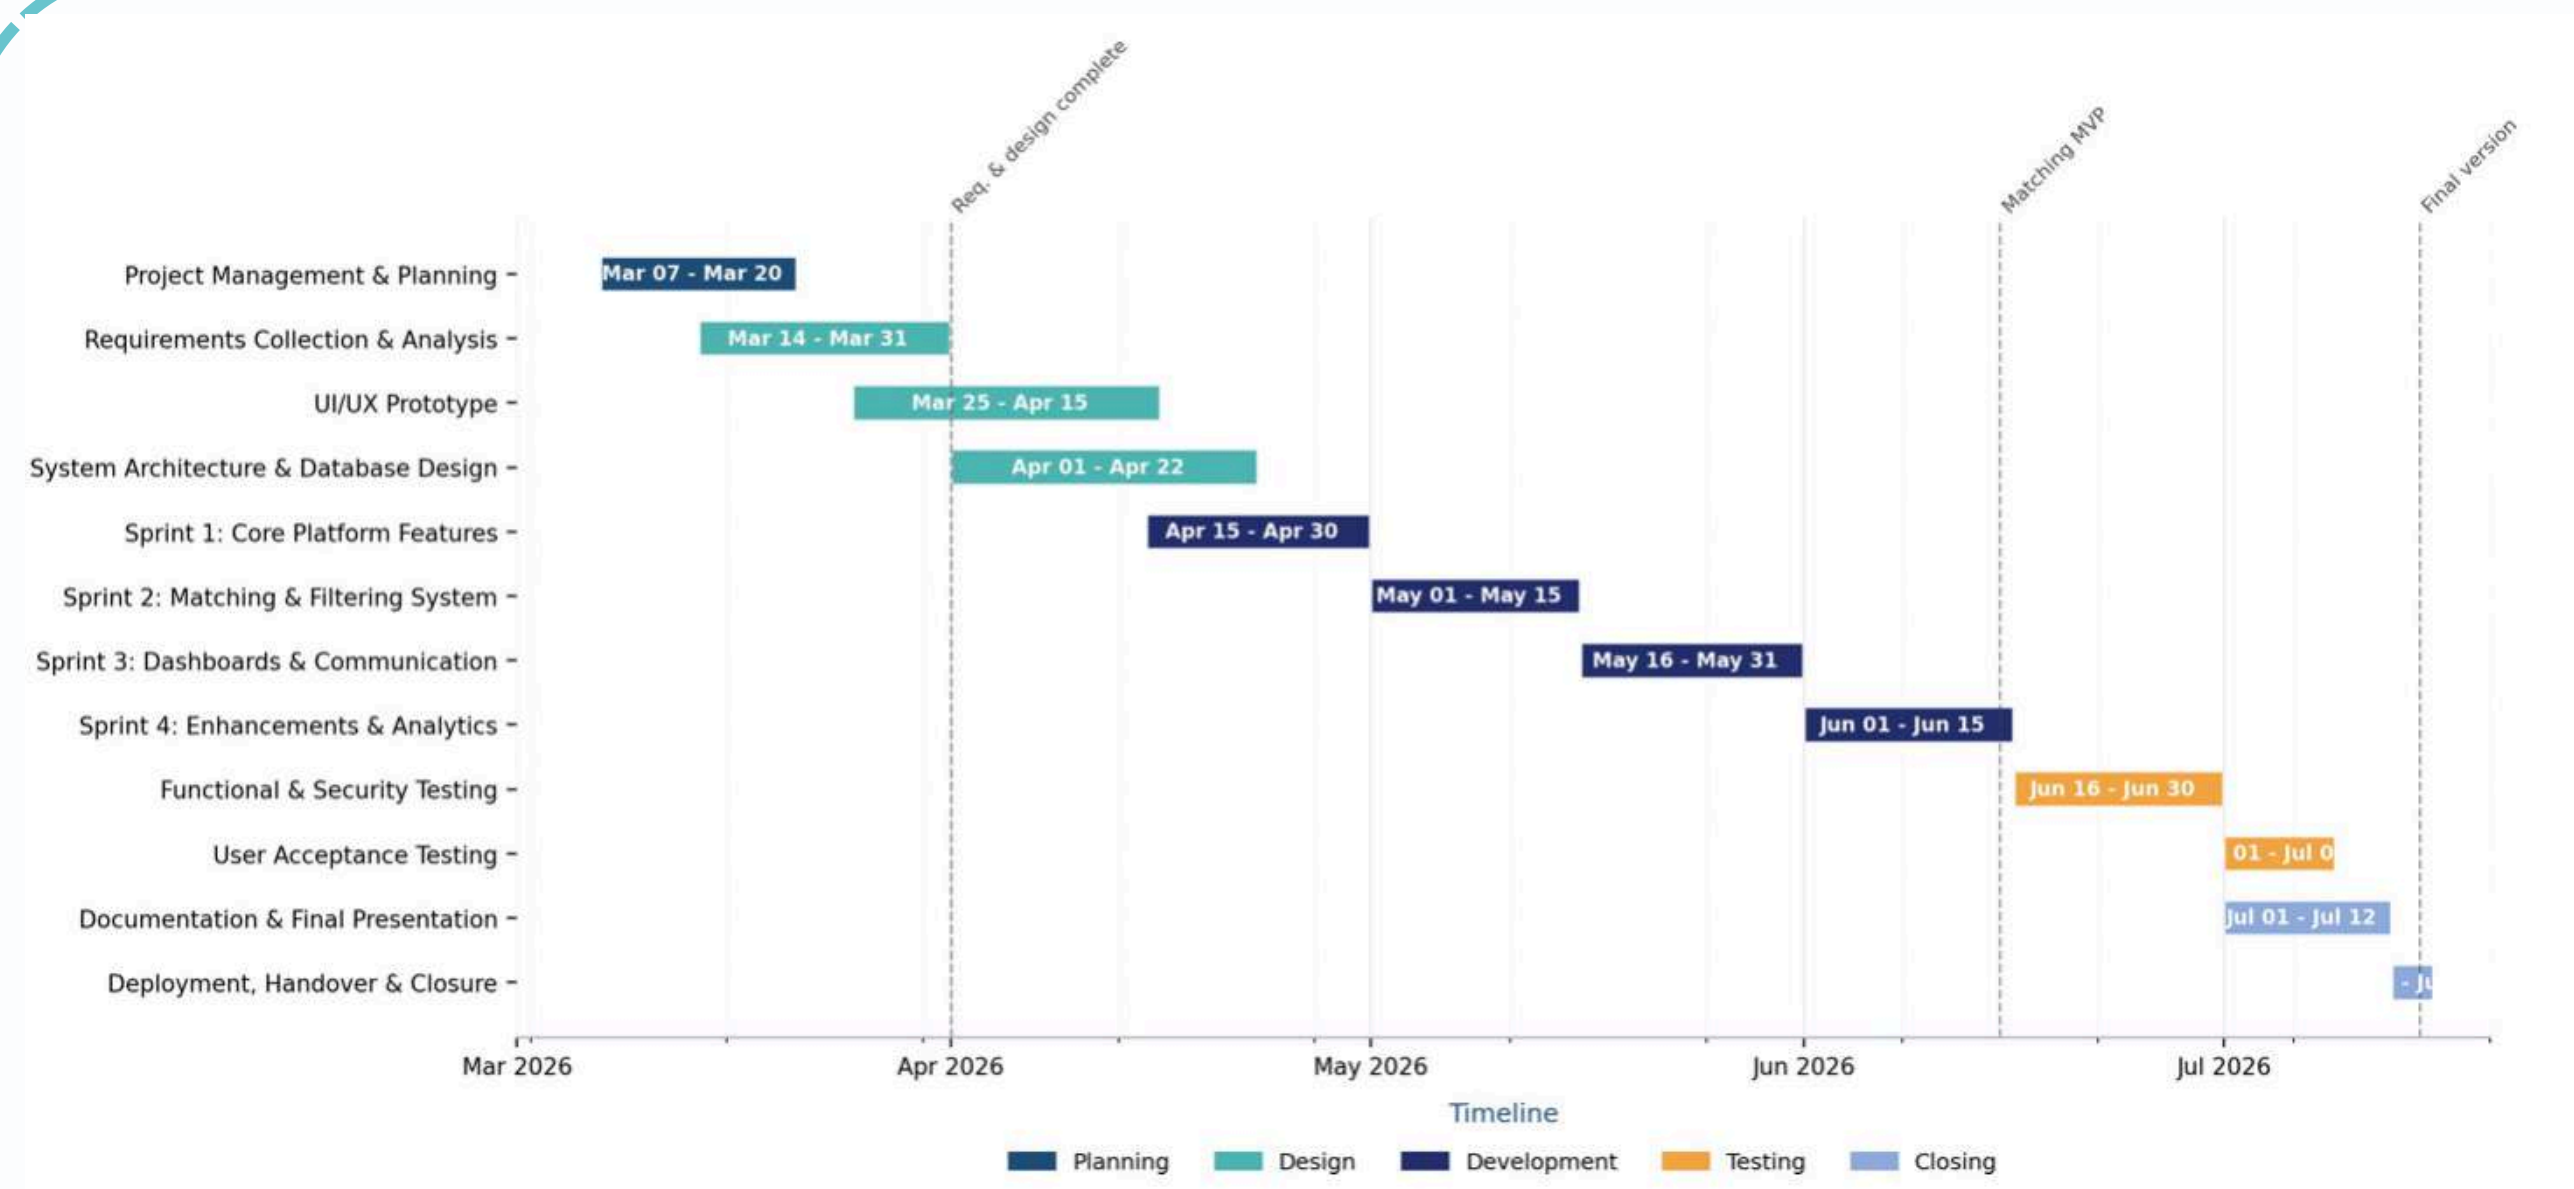

Milestone	Planned Date	Related Deliverable
Requirements and system design completed	April 1, 2026	Approved requirements, UI/UX prototype, and system architecture
Matching engine and MVP completed	June 15, 2026	Core platform, smart matching, filtering, dashboards, and notifications
Pilot testing and final production version	July 15, 2026	Testing, documentation, deployment, handover, and project closure

Risk Register

ID	Type	Risk Description	Likelihood	Impact	Severity	Owner	Risk Response Strategy
R01	Negative	Data Privacy Breach: Unauthorized access to startups' business plans or investors' financial profiles.	Low	High	High	Security Lead	Implement AES-256 encryption and multi-factor authentication (MFA) for all users.
R02	Negative	Algorithm Inaccuracy: The matching engine fails to connect entrepreneurs with the right investors.	Medium	High	High	Backend Developer	Conduct extensive testing of the matching logic and refine parameters based on user feedback.
R03	Negative	Low User Trust: Investors may hesitate to use the platform if startup ideas are not properly vetted.	Medium	Medium	Medium	QA Specialist	Establish a strict verification process for all uploaded business proposals before they go live.
R04	Negative	System Scalability: The Sella platform crashes due to a sudden surge in concurrent users/investors.	Low	High	High	DevOps Team	Use cloud hosting with auto-scaling features to handle traffic spikes during peak hours.
R05	Positive	High Adoption Rate: A higher-than-expected number of startups register within the first month.	Medium	High	Opportunity	Marketing Lead	Develop an expansion plan to increase support staff and server capacity to maintain quality.
R06	Positive	Government Partnerships: Potential collaboration with Saudi entrepreneurship hubs (e.g., Monsha'at).	Low	High	Opportunity	Project Manager	Prepare professional API documentation to allow seamless integration with governmental systems.
R07	Negative	Scope Creep: Adding extra features not in the initial MVP, leading to a delay in the July 2026 launch.	High	Medium	High	Project Manager	Stick strictly to the Sprint backlog and defer new requests to the post-launch phase.

Conclusion

In conclusion, Sella is more than just a matching app; it is a strategic bridge designed to empower PNU entrepreneurs and simplify the investment process. By combining smart technology with high-security standards, we aim to transform the local startup ecosystem and contribute to the goals of Saudi Vision 2030. Thank you for your time.
